

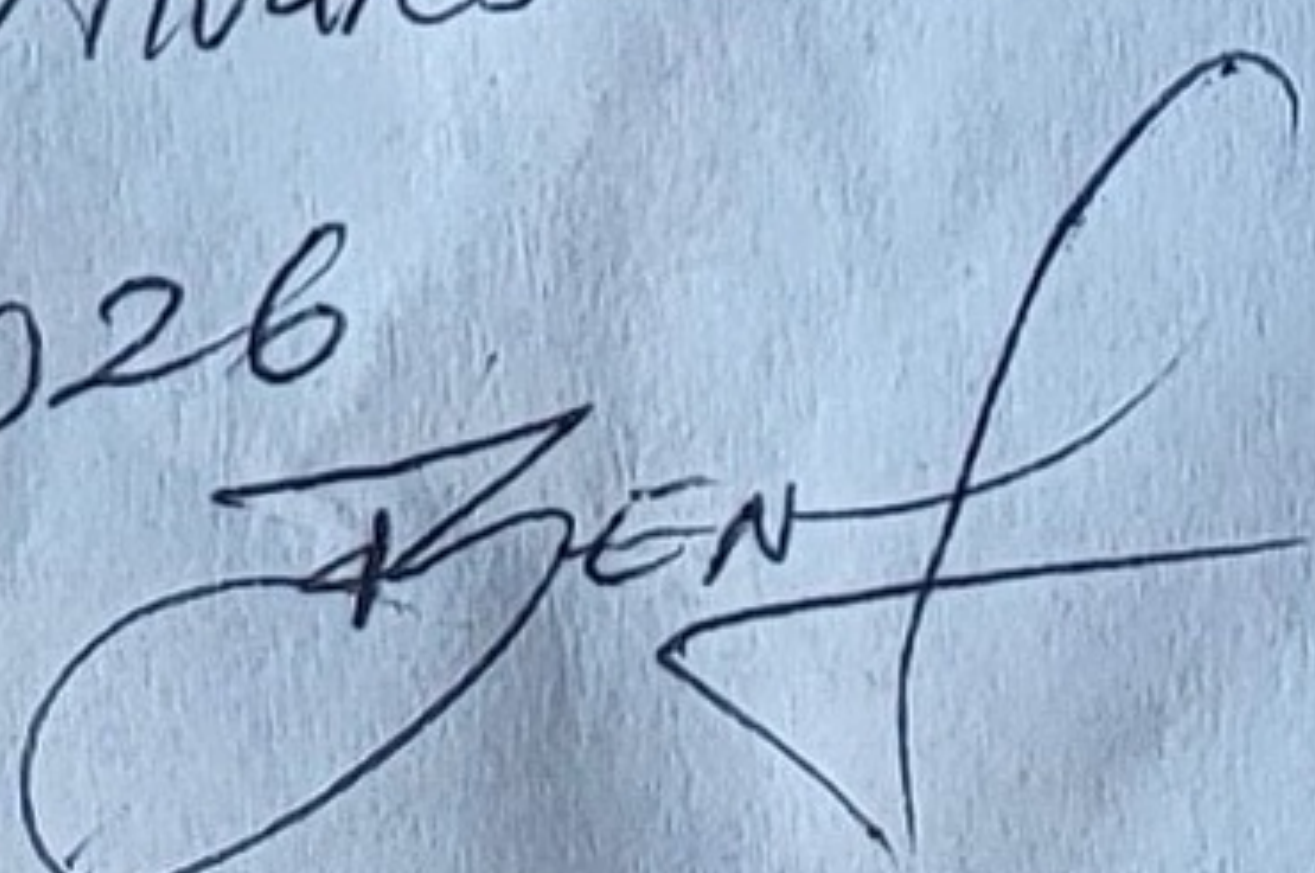
JD FIELDS AND COMPANY
PIPE TALLY

Customer Order No.
Size 24.000" OD x 0.375" Wall
Specification ASTM A252 Grade 3
Pipe Type HFW
Nominal Weight 94.71 lb/ft
Joint Length 20.00 ft (each)
Date

Joint No.	Heat No.	OD (in)	Wall (in)	Length (ft)	Weight (lb/ft)	Total Weight (lbs)
1	D03803	24	0.375	20	94.71	1,894.20
2	D20233	24	0.375	20	94.71	1,894.20
3	D20234	24	0.375	20	94.71	1,894.20
4	D20236	24	0.375	20	94.71	1,894.20
5	D20495	24	0.375	20	94.71	1,894.20
				Total	100	9,471.00

NOTE: Heat numbers pulled from American Steel Pipe Qualification Report (Cust. Order 062526-BS, ASP Order 2646, 24.00 x .375 HFW ASTM A252 Gr 3). That report certifies the full shipment (ship no. 620617 to 621229) across 17 heats and does not map individual heats to individual joints, so the 5 heats above are assigned in listed order as placeholders, not verified against physical joints. Confirm against the actual joint tags before this goes final.

NOTE: The Houston Tubulars receiving report also attached (RH 3507, PO 61-110290-4) is a different product, 24" OD x 0.750" wall, Grade X65, DSAW, 2 pieces at 40 ft, and lists no heat numbers, so it could not be used as a heat source for this tally.

Pablo Alvarez
08-18-2026


Pablo Alvarez
